ID	Task Name	Duration	Start	Finish
1				
2	**PRE-CONSTRUCTION ACTIVITIES**	17 days	Tue 9/27/11	Wed 10/19/11
3	Pre-Construction Meeting	1 day	Tue 9/27/11	Tue 9/27/11
4	Prepare Submittals & Traffic Control	5 days	Wed 9/28/11	Tue 10/4/11
5	Staking Request	3 days	Wed 9/28/11	Fri 9/30/11
6	Notice to proceed	1 day	Wed 10/5/11	Wed 10/5/11
7	Distribute Door Hangers	1 day	Mon 10/3/11	Mon 10/3/11
8	Preconstruction Video Documentation	1 day	Fri 10/7/11	Fri 10/7/11
9	Mobilization	1 day	Fri 10/7/11	Fri 10/7/11
10	Clean & Pre-CCTV Exist. Mains (Sheets 2, 5, 11, 9)	2 days	Mon 10/10/11	Tue 10/11/11
11				
12	**SHEETS 2 & 3 - Alta Way, Mira Monte & Beaumont**	11 days	Wed 10/12/11	Wed 10/26/11
13	Sawcutting, Setting BMP's, Potholing	2 days	Wed 10/12/11	Thu 10/13/11
14	Dig, Lay, Backfill 10" Sewer Main from exist. MH on Alta Way up to MH#4, L=200.50 Lf	1.5 days	Fri 10/14/11	Mon 10/17/11
15	Dig, Lay, Backfill 10" SDR26 Main from MH 4 to MH 5 on Mira Monte, L=194 Lf	1.5 days	Mon 10/17/11	Tue 10/18/11
16	Dig, Lay, Backfill 8" Sewer Main on Beaumont Ave, L=374 Lf	3 days	Wed 10/19/11	Fri 10/21/11
17	Dig, Lay, Backfill 8" SDR35 Main, Alley off of Camino De La Costa, L=138 Lf	1 day	Mon 10/24/11	Mon 10/24/11
18	Install Sewer Laterals, 9ea	2 days	Tue 10/25/11	Wed 10/26/11
19				
20	**SHEETS 5 & 4 - DOLPHIN PLACE**	13 days	Thu 10/27/11	Tue 11/15/11
21	Dig, Lay, Backfill 8" SDR26 Main, L=1160 Lf	7 days	Thu 10/27/11	Fri 11/4/11
22	Install Sewer Laterals, 39ea	6 days	Mon 11/7/11	Tue 11/15/11
23				
24	**SHEET 6 - ABALONE PLACE**	5 days	Wed 11/16/11	Tue 11/22/11
25	Dig, Lay, Backfill 8" Sewer Main, L=750 Lf	4 days	Wed 11/16/11	Mon 11/21/11
26	Install Sewer Laterals, 5ea	1 day	Tue 11/22/11	Tue 11/22/11
27				
28	**CCTV & Paving - Sheets 2 & 3**	4 days	Wed 11/23/11	Wed 11/30/11
29	Wayneball, Air Test, CCTV Inspection - 769 Lf	2 days	Wed 11/23/11	Mon 11/28/11
30	Remove Coldmix and PCC Cap	2 days	Tue 11/29/11	Wed 11/30/11
31				
32	**SHEET 11 - CALUMET AVE. & FORWARD ST.**	12 days	Thu 12/1/11	Fri 12/16/11
33	Dig, Lay, Backfill 8" SDR35 Main, L=806 Lf	6 days	Thu 12/1/11	Thu 12/8/11
34	Install Sewer Laterals, 27ea	6 days	Fri 12/9/11	Fri 12/16/11
35				
36	**CCTV & Paving - Sheets 4, 5 & 6**	5 days	Mon 12/19/11	Fri 12/23/11
37	Wayneball, Air Test, CCTV Inspection - 1910 Lf	2 days	Mon 12/19/11	Tue 12/20/11
38	Remove Coldmix and PCC Cap	3 days	Wed 12/21/11	Fri 12/23/11
39				
40	**SHEET 7 - LA JOLLA HERMOSA AVE.**	8 days	Tue 12/27/11	Fri 1/6/12
41	Dig, Lay, Backfill 8" SDR35 Main, L=590 Lf	4 days	Tue 12/27/11	Fri 12/30/11
42	Install Sewer Laterals, 21ea	4 days	Tue 1/3/12	Fri 1/6/12
43				
44	**SHEET 8 - LA JOLLA HERMOSA AVE.**	8 days	Mon 1/9/12	Thu 1/19/12
45	Dig, Lay, Backfill 8" SDR35 Main, L=570 Lf	4 days	Mon 1/9/12	Thu 1/12/12

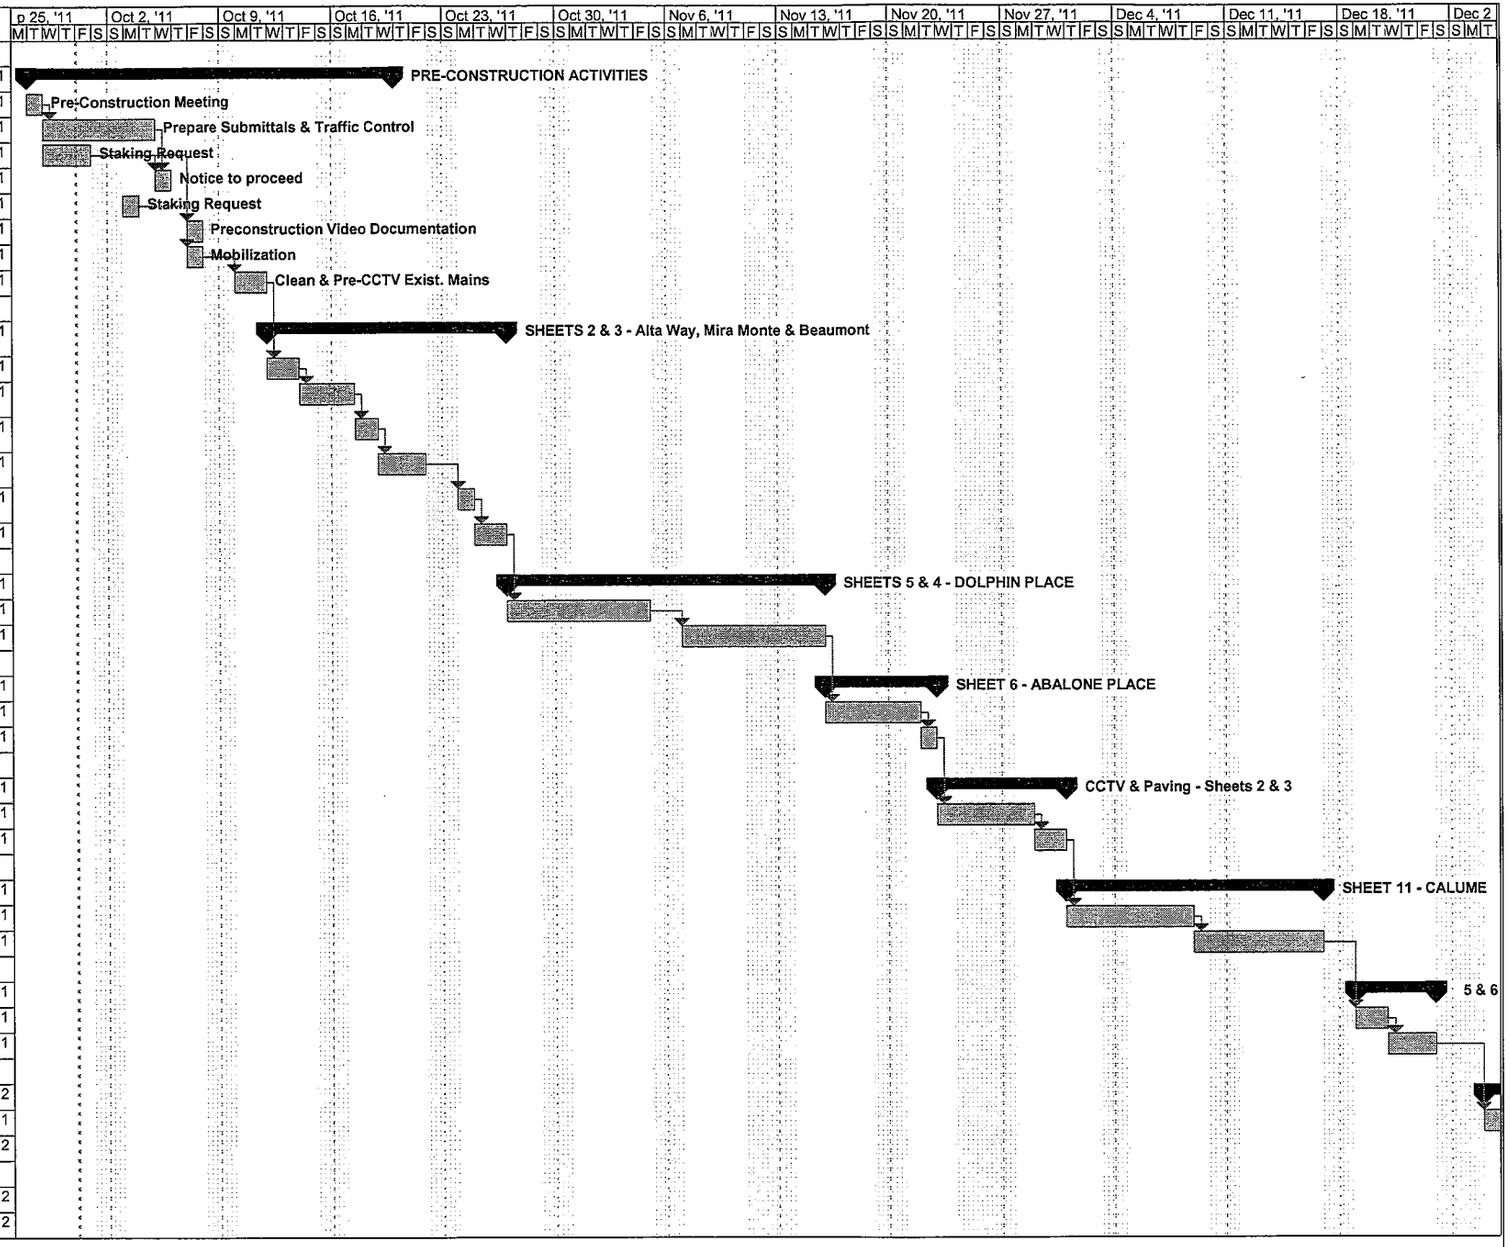

Project: SEWER GROUP JOB 714
Burtech Pipeline, Inc.
Date: Fri 9/30/11

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name	Duration	Start	Finish
46	Install Sewer Laterals, 22ea	5 days	Fri 1/13/12	Fri 1/20/12
47				
48	**SHEET 9 - BEAUMONT AVENUE**	8 days	Mon 1/23/12	Wed 2/1/12
49	Dig, Lay, Backfill 8" Sewer Main, L=680 Lf	4 days	Mon 1/23/12	Thu 1/26/12
50	Install Sewer Laterals, 21ea	4 days	Fri 1/27/12	Wed 2/1/12
51				
52	**CCTV & Paving - Sheets 11 & 7**	5 days	Thu 2/2/12	Wed 2/8/12
53	Wayneball, Air Test, CCTV Inspection - 1396 Lf	2 days	Thu 2/2/12	Fri 2/3/12
54	Remove Coldmix and PCC Cap	3 days	Mon 2/6/12	Wed 2/8/12
55				
56	**SHEET 10 - BELLEVUE AVENUE**	8 days	Thu 2/9/12	Tue 2/21/12
57	Pipe Bursting 8" Sewer Main, L=250 Lf	2 days	Thu 2/9/12	Fri 2/10/12
58	Dig, Lay, Backfill 8" SDR35 Main, L=347 Lf	2 days	Mon 2/13/12	Tue 2/14/12
59	Install Sewer Laterals, 21ea	4 days	Wed 2/15/12	Tue 2/21/12
60				
61	**CCTV & Paving - Sheets 8 & 9**	5 days	Wed 2/22/12	Tue 2/28/12
62	Wayneball, Air Test, CCTV Inspection - 1250 Lf	2 days	Wed 2/22/12	Thu 2/23/12
63	Remove Coldmix and PCC Cap	3 days	Fri 2/24/12	Tue 2/28/12
64				
65	**SHEET 12 - BONAIR WAY (ALLEY)**	8 days	Wed 2/29/12	Fri 3/9/12
66	Dig, Lay, Backfill 8" Sewer Main, L=475 Lf	4 days	Wed 2/29/12	Mon 3/5/12
67	Install Sewer Laterals, 23ea	4 days	Tue 3/6/12	Fri 3/9/12
68				
69	**CCTV & Paving - Sheets 10 & 12**	5 days	Mon 3/12/12	Fri 3/16/12
70	Wayneball, Air Test, CCTV Inspection - 1072 Lf	2 days	Mon 3/12/12	Tue 3/13/12
71	Remove Coldmix and PCC Cap	3 days	Wed 3/14/12	Fri 3/16/12
72				
73	**TUNNELING & REPLUMBING**	30 days	Mon 3/19/12	Fri 4/27/12
74	Sheet 13 La Jolla Hermosa Ave, 8ea	16 days	Mon 3/19/12	Mon 4/9/12
75	Sheet 3 Alta Way, 1ea	2 days	Tue 4/10/12	Wed 4/11/12
76	Sheet 6 Abalone Place, 5ea	10 days	Thu 4/12/12	Wed 4/25/12
77	Sheet 14 Dolphin, 1ea	2 days	Thu 4/26/12	Fri 4/27/12
78				
79	**MISCELLANEOUS. WORKS**	47 days	Mon 4/9/12	Tue 6/12/12
80	Sewer Main Rehabilitation on Sheet 3, L=139 Lf	2 days	Mon 4/9/12	Tue 4/10/12
81	Curb Ramps, 36 Ea	10 days	Wed 4/11/12	Tue 4/24/12
82	AC Paving & Overlay	6 days	Wed 4/25/12	Wed 5/2/12
83	Slurry Sealing	2 days	Thu 5/3/12	Fri 5/4/12
84	Striping	3 days	Mon 5/21/12	Wed 5/23/12
85	Initial Walkthrough Inspection	2 days	Thu 5/24/12	Fri 5/25/12
86	Punchlist Corrections	10 days	Mon 5/28/12	Fri 6/8/12
87	Final Walkthrough Inspection	2 days	Mon 6/11/12	Tue 6/12/12



Project: SEWER GROUP JOB 714
Burtech Pipeline, Inc.
Date: Fri 9/30/11

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name	Duration	Start	Finish
1				
2	**PRE-CONSTRUCTION ACTIVITIES**	17 days	Tue 9/27/11	Wed 10/19/11
3	Pre-Construction Meeting	1 day	Tue 9/27/11	Tue 9/27/11
4	Prepare Submittals & Traffic Control	5 days	Wed 9/28/11	Tue 10/4/11
5	Staking Request	3 days	Wed 9/28/11	Fri 9/30/11
6	Notice to proceed	1 day	Wed 10/5/11	Wed 10/5/11
7	Distribute Door Hangers	1 day	Mon 10/3/11	Mon 10/3/11
8	Preconstruction Video Documentation	1 day	Fri 10/7/11	Fri 10/7/11
9	Mobilization	1 day	Fri 10/7/11	Fri 10/7/11
10	Clean & Pre-CCTV Exist. Mains (Sheets 2, 5, 11, 9)	2 days	Mon 10/10/11	Tue 10/11/11
11				
12	**SHEETS 2 & 3 - Alta Way, Mira Monte & Beaumont**	11 days	Wed 10/12/11	Wed 10/26/11
13	Sawcutting, Setting BMP's, Potholing	2 days	Wed 10/12/11	Thu 10/13/11
14	Dig, Lay, Backfill 10" Sewer Main from exist. MH on Alta Way up to MH#4, L=200.50 Lf	1.5 days	Fri 10/14/11	Mon 10/17/11
15	Dig, Lay, Backfill 10" SDR26 Main from MH 4 to MH 5 on Mira Monte, L=194 Lf	1.5 days	Mon 10/17/11	Tue 10/18/11
16	Dig, Lay, Backfill 8" Sewer Main on Beaumont Ave, L=374 Lf	3 days	Wed 10/19/11	Fri 10/21/11
17	Dig, Lay, Backfill 8" SDR35 Main, Alley off of Camino De La Costa, L=138 Lf	1 day	Mon 10/24/11	Mon 10/24/11
18	Install Sewer Laterals, 9ea	2 days	Tue 10/25/11	Wed 10/26/11
19				
20	**SHEETS 5 & 4 - DOLPHIN PLACE**	13 days	Thu 10/27/11	Tue 11/15/11
21	Dig, Lay, Backfill 8" SDR26 Main, L=1160 Lf	7 days	Thu 10/27/11	Fri 11/4/11
22	Install Sewer Laterals, 39ea	6 days	Mon 11/7/11	Tue 11/15/11
23				
24	**SHEET 6 - ABALONE PLACE**	5 days	Wed 11/16/11	Tue 11/22/11
25	Dig, Lay, Backfill 8" Sewer Main, L=750 Lf	4 days	Wed 11/16/11	Mon 11/21/11
26	Install Sewer Laterals, 5ea	1 day	Tue 11/22/11	Tue 11/22/11
27				
28	**CCTV & Paving - Sheets 2 & 3**	4 days	Wed 11/23/11	Wed 11/30/11
29	Wayneball, Air Test, CCTV Inspection - 769 Lf	2 days	Wed 11/23/11	Mon 11/28/11
30	Remove Coldmix and PCC Cap	2 days	Tue 11/29/11	Wed 11/30/11
31				
32	**SHEET 11 - CALUMET AVE. & FORWARD ST.**	12 days	Thu 12/1/11	Fri 12/16/11
33	Dig, Lay, Backfill 8" SDR35 Main, L=806 Lf	6 days	Thu 12/1/11	Thu 12/8/11
34	Install Sewer Laterals, 27ea	6 days	Fri 12/9/11	Fri 12/16/11
35				
36	**CCTV & Paving - Sheets 4, 5 & 6**	5 days	Mon 12/19/11	Fri 12/23/11
37	Wayneball, Air Test, CCTV Inspection - 1910 Lf	2 days	Mon 12/19/11	Tue 12/20/11
38	Remove Coldmix and PCC Cap	3 days	Wed 12/21/11	Fri 12/23/11
39				
40	**SHEET 7 - LA JOLLA HERMOSA AVE.**	8 days	Tue 12/27/11	Fri 1/6/12
41	Dig, Lay, Backfill 8" SDR35 Main, L=590 Lf	4 days	Tue 12/27/11	Fri 12/30/11
42	Install Sewer Laterals, 21ea	4 days	Tue 1/3/12	Fri 1/6/12
43				
44	**SHEET 8 - LA JOLLA HERMOSA AVE.**	8 days	Mon 1/9/12	Thu 1/19/12
45	Dig, Lay, Backfill 8" SDR35 Main, L=570 Lf	4 days	Mon 1/9/12	Thu 1/12/12

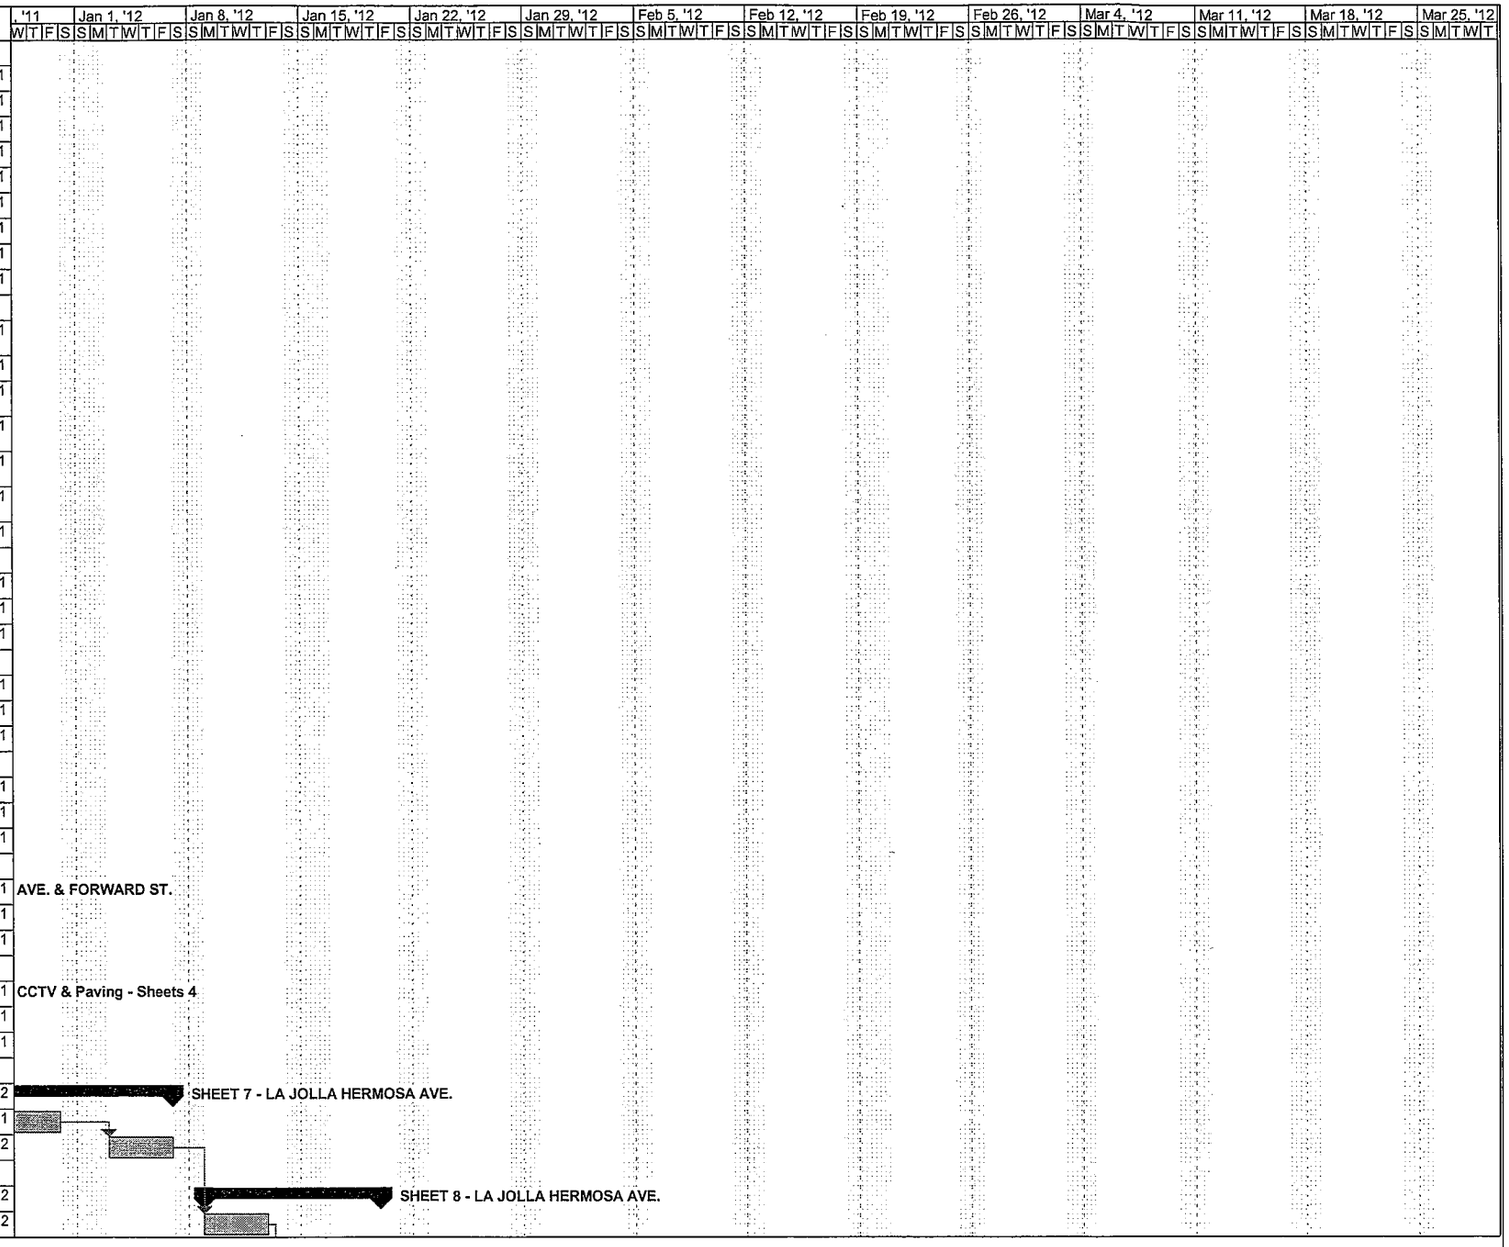

Project: SEWER GROUP JOB 714
Burtech Pipeline, Inc.
Date: Fri 9/30/11

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name	Duration	Start	Finish
46	Install Sewer Laterals, 22ea	5 days	Fri 1/13/12	Fri 1/20/12
47				
48	**SHEET 9 - BEAUMONT AVENUE**	8 days	Mon 1/23/12	Wed 2/1/12
49	Dig, Lay, Backfill 8" Sewer Main, L=680 Lf	4 days	Mon 1/23/12	Thu 1/26/12
50	Install Sewer Laterals, 21ea	4 days	Fri 1/27/12	Wed 2/1/12
51				
52	**CCTV & Paving - Sheets 11 & 7**	5 days	Thu 2/2/12	Wed 2/8/12
53	Wayneball, Air Test, CCTV Inspection - 1396 Lf	2 days	Thu 2/2/12	Fri 2/3/12
54	Remove Coldmix and PCC Cap	3 days	Mon 2/6/12	Wed 2/8/12
55				
56	**SHEET 10 - BELLEVUE AVENUE**	8 days	Thu 2/9/12	Tue 2/21/12
57	Pipe Bursting 8" Sewer Main, L=250 Lf	2 days	Thu 2/9/12	Fri 2/10/12
58	Dig, Lay, Backfill 8" SDR35 Main, L=347 Lf	2 days	Mon 2/13/12	Tue 2/14/12
59	Install Sewer Laterals, 21ea	4 days	Wed 2/15/12	Tue 2/21/12
60				
61	**CCTV & Paving - Sheets 8 & 9**	5 days	Wed 2/22/12	Tue 2/28/12
62	Wayneball, Air Test, CCTV Inspection - 1250 Lf	2 days	Wed 2/22/12	Thu 2/23/12
63	Remove Coldmix and PCC Cap	3 days	Fri 2/24/12	Tue 2/28/12
64				
65	**SHEET 12 - BONAIR WAY (ALLEY)**	8 days	Wed 2/29/12	Fri 3/9/12
66	Dig, Lay, Backfill 8" Sewer Main, L=475 Lf	4 days	Wed 2/29/12	Mon 3/5/12
67	Install Sewer Laterals, 23ea	4 days	Tue 3/6/12	Fri 3/9/12
68				
69	**CCTV & Paving - Sheets 10 & 12**	5 days	Mon 3/12/12	Fri 3/16/12
70	Wayneball, Air Test, CCTV Inspection - 1072 Lf	2 days	Mon 3/12/12	Tue 3/13/12
71	Remove Coldmix and PCC Cap	3 days	Wed 3/14/12	Fri 3/16/12
72				
73	**TUNNELING & REPLUMBING**	30 days	Mon 3/19/12	Fri 4/27/12
74	Sheet 13 La Jolla Hermosa Ave, 8ea	16 days	Mon 3/19/12	Mon 4/9/12
75	Sheet 3 Alta Way, 1ea	2 days	Tue 4/10/12	Wed 4/11/12
76	Sheet 6 Abalone Place, 5ea	10 days	Thu 4/12/12	Wed 4/25/12
77	Sheet 14 Dolphin, 1ea	2 days	Thu 4/26/12	Fri 4/27/12
78				
79	**MISCELLANEOUS. WORKS**	47 days	Mon 4/9/12	Tue 6/12/12
80	Sewer Main Rehabilitation on Sheet 3, L=139 Lf	2 days	Mon 4/9/12	Tue 4/10/12
81	Curb Ramps, 36 Ea	10 days	Wed 4/11/12	Tue 4/24/12
82	AC Paving & Overlay	6 days	Wed 4/25/12	Wed 5/2/12
83	Slurry Sealing	2 days	Thu 5/3/12	Fri 5/4/12
84	Striping	3 days	Mon 5/21/12	Wed 5/23/12
85	Initial Walkthrough Inspection	2 days	Thu 5/24/12	Fri 5/25/12
86	Punchlist Corrections	10 days	Mon 5/28/12	Fri 6/8/12
87	Final Walkthrough Inspection	2 days	Mon 6/11/12	Tue 6/12/12

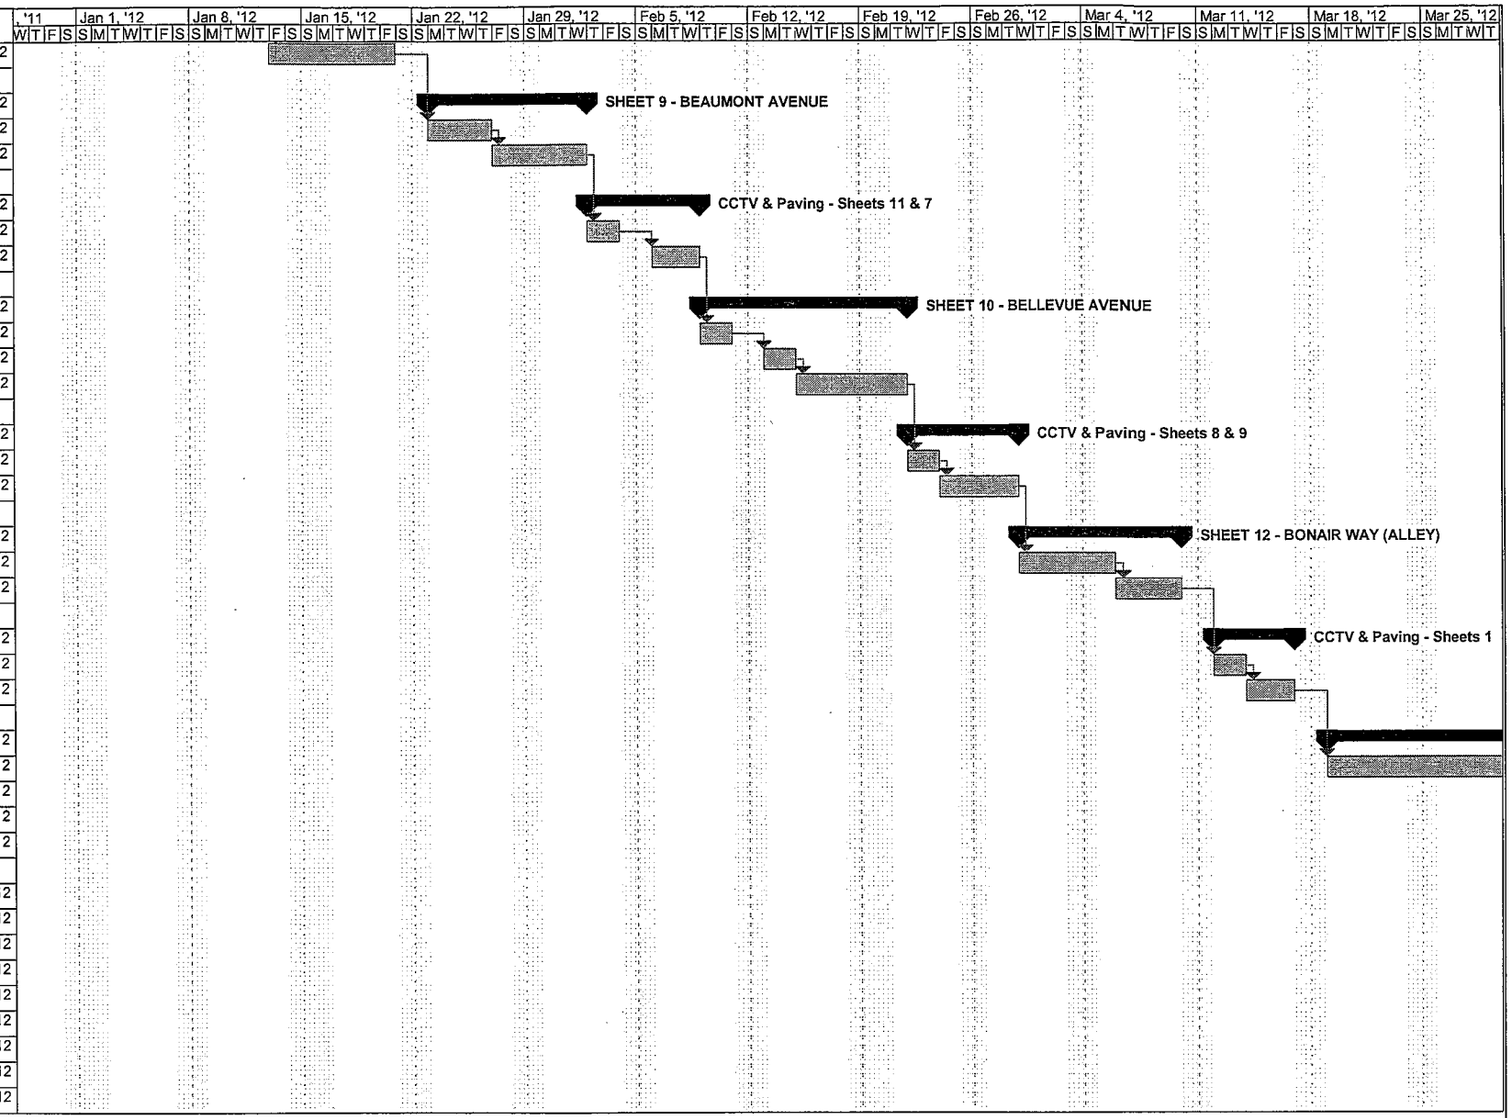

Project: SEWER GROUP JOB 714
Burtech Pipeline, Inc.
Date: Fri 9/30/11

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name	Duration	Start	Finish
46	Install Sewer Laterals, 22ea	5 days	Fri 1/13/12	Fri 1/20/12
47				
48	**SHEET 9 - BEAUMONT AVENUE**	8 days	Mon 1/23/12	Wed 2/1/12
49	Dig, Lay, Backfill 8" Sewer Main, L=680 Lf	4 days	Mon 1/23/12	Thu 1/26/12
50	Install Sewer Laterals, 21ea	4 days	Fri 1/27/12	Wed 2/1/12
51				
52	**CCTV & Paving - Sheets 11 & 7**	5 days	Thu 2/2/12	Wed 2/8/12
53	Wayneball, Air Test, CCTV Inspection - 1396 Lf	2 days	Thu 2/2/12	Fri 2/3/12
54	Remove Coldmix and PCC Cap	3 days	Mon 2/6/12	Wed 2/8/12
55				
56	**SHEET 10 - BELLEVUE AVENUE**	8 days	Thu 2/9/12	Tue 2/21/12
57	Pipe Bursting 8" Sewer Main, L=250 Lf	2 days	Thu 2/9/12	Fri 2/10/12
58	Dig, Lay, Backfill 8" SDR35 Main, L=347 Lf	2 days	Mon 2/13/12	Tue 2/14/12
59	Install Sewer Laterals, 21ea	4 days	Wed 2/15/12	Tue 2/21/12
60				
61	**CCTV & Paving - Sheets 8 & 9**	5 days	Wed 2/22/12	Tue 2/28/12
62	Wayneball, Air Test, CCTV Inspection - 1250 Lf	2 days	Wed 2/22/12	Thu 2/23/12
63	Remove Coldmix and PCC Cap	3 days	Fri 2/24/12	Tue 2/28/12
64				
65	**SHEET 12 - BONAIR WAY (ALLEY)**	8 days	Wed 2/29/12	Fri 3/9/12
66	Dig, Lay, Backfill 8" Sewer Main, L=475 Lf	4 days	Wed 2/29/12	Mon 3/5/12
67	Install Sewer Laterals, 23ea	4 days	Tue 3/6/12	Fri 3/9/12
68				
69	**CCTV & Paving - Sheets 10 & 12**	5 days	Mon 3/12/12	Fri 3/16/12
70	Wayneball, Air Test, CCTV Inspection - 1072 Lf	2 days	Mon 3/12/12	Tue 3/13/12
71	Remove Coldmix and PCC Cap	3 days	Wed 3/14/12	Fri 3/16/12
72				
73	**TUNNELING & REPLUMBING**	30 days	Mon 3/19/12	Fri 4/27/12
74	Sheet 13 La Jolla Hermosa Ave, 8ea	16 days	Mon 3/19/12	Mon 4/9/12
75	Sheet 3 Alta Way, 1ea	2 days	Tue 4/10/12	Wed 4/11/12
76	Sheet 6 Abalone Place, 5ea	10 days	Thu 4/12/12	Wed 4/25/12
77	Sheet 14 Dolphin, 1ea	2 days	Thu 4/26/12	Fri 4/27/12
78				
79	**MISCELLANEOUS. WORKS**	47 days	Mon 4/9/12	Tue 6/12/12
80	Sewer Main Rehabilitation on Sheet 3, L=139 Lf	2 days	Mon 4/9/12	Tue 4/10/12
81	Curb Ramps, 36 Ea	10 days	Wed 4/11/12	Tue 4/24/12
82	AC Paving & Overlay	6 days	Wed 4/25/12	Wed 5/2/12
83	Slurry Sealing	2 days	Thu 5/3/12	Fri 5/4/12
84	Striping	3 days	Mon 5/21/12	Wed 5/23/12
85	Initial Walkthrough Inspection	2 days	Thu 5/24/12	Fri 5/25/12
86	Punchlist Corrections	10 days	Mon 5/28/12	Fri 6/8/12
87	Final Walkthrough Inspection	2 days	Mon 6/11/12	Tue 6/12/12

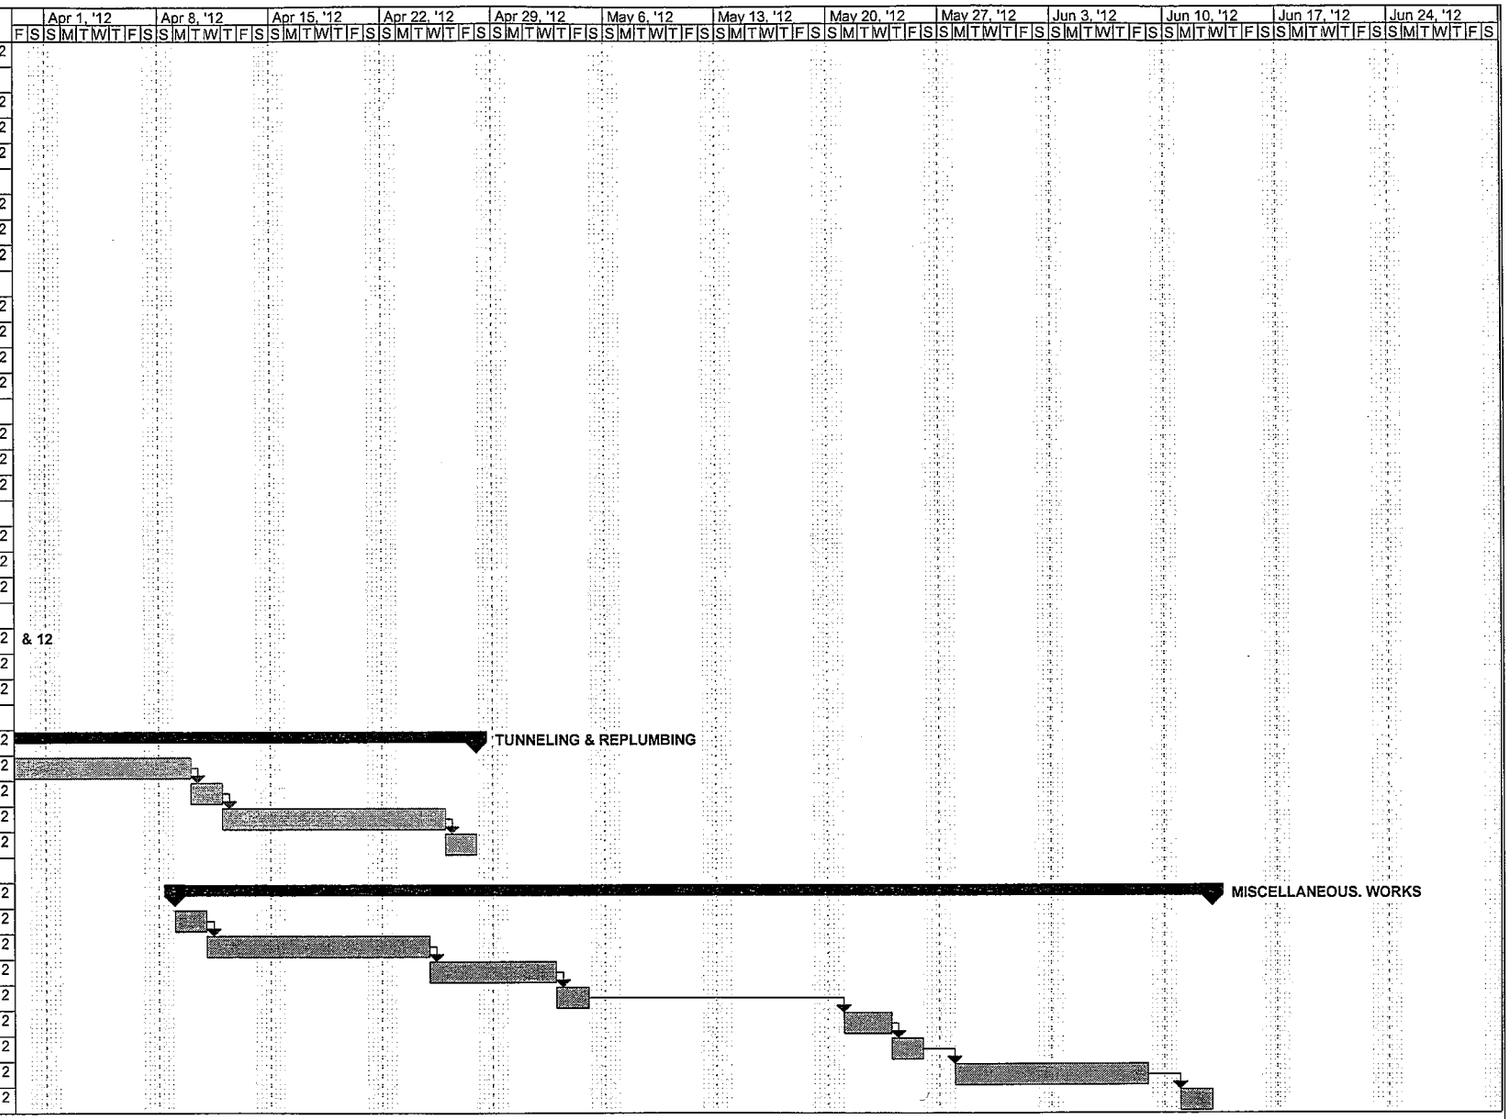

Project: SEWER GROUP JOB 714
Burtech Pipeline, Inc.
Date: Fri 9/30/11

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
